N

TEMPORARY, SECURE FENCING AROUND ENTIRE PERIMETER OF TEMPORARY CONSTRUCTION COMPOUND

HARDCORE ACCESS ROAD AROUND COMPOUND

WELFARE FACILITIES

SECURE LOCK UP CONTAINERS

SITE OFFICES

DESIGNATED PARKING AREA

18m LW PIPE 4 HIGH 214 LENGTHS

18m LW PIPE 4 HIGH 214 LENGTHS

18m LW PIPE 4 HIGH 214 LENGTHS

18m LW PIPE 4 HIGH 214 LENGTHS

MATERIAL LAYDOWN AREA

12m LW PIPE 4 HIGH 324 LENGTHS

MATERIAL LAYDOWN AREA

12m HW PIPE 4 HIGH 245 LENGTHS

18m HW PIPE 4 HIGH 109 LENGTHS

TEMPORARY CONSTRUCTION COMPOUND

BEND STORAGE AREA

BEND STORAGE AREA

8m WIDE, SECURE DOUBLE ACCESS GATE

MATERIAL STORAGE AREA

CRANE AND TRUCK PARKING

ACCESS LANE GIVING SITE AGGESS/EGRESS TO PUBLIC ROAD R441

0 10 20 30 40 50m

TEMPORARY CONSTRUCTION COMPOUND 03
LAYOUT
(Scale 1:500)

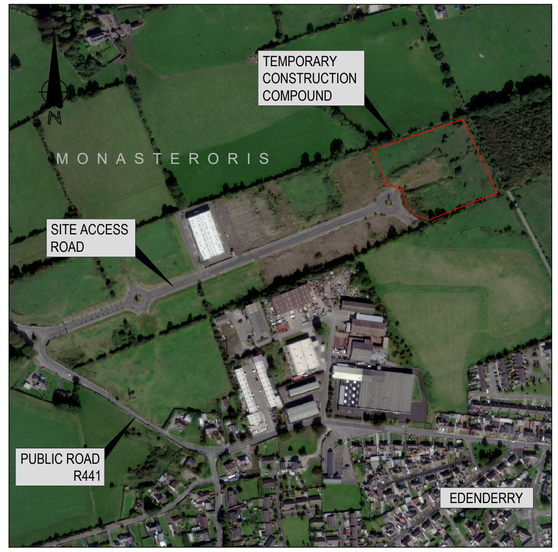

TEMPORARY CONSTRUCTION COMPOUND 03
LOCATION PLAN
(Scale 1:5,000)

NOTES:

1. THIS DRAWING IS FOR PLANNING PURPOSES ONLY. LINEPIPE QUANTITIES TO BE CONFIRMED.
2. DO NOT SCALE FROM THIS DRAWING.
3. SITE OFFICES, WELFARE FACILITIES AND SECURE LOCK UP CONTAINERS ARE SHOWN INDICITAVELY ONLY, AND SUBJECT TO CHANGE.
4. CONTRACTOR TO DETERMINE TEMPORARY SITE LAYOUT. DESIGN SHOWN INDICATIVELY ONLY. PIPE HANDLING, TRANSPORT AND STORAGE SHALL BE IN ACCORDANCE WITH AD/SP/007, AND IGEM/TD1 SUPPLEMENT 1, Ed.2.
5. CONTRACTOR TO DETERMINE LOCATION OF EXISTING SERVICES WITHIN PROPOSED TEMPORARY CONSTRUCTION COMPOUND. ALL SERVICES WITHIN TEMPORARY CONSTRUCTION COMPOUND TO BE PROTECTED ADEQUATELY FROM HEAVY MACHINERY, ETC.
6. PIPE LENGTH ASSUMED TO BE 12m AND 18m. PIPE STORAGE AREAS SHOW PIPES STACKED 4Nos. HIGH. 24,200m OF PIPE STORAGE SHOWN.

LEGEND:

TEMPORARY CONSTRUCTION COMPOUND

DESIGNATED PARKING AREA

PLANNING ISSUE

ISSUE	REVISION	REV. BY	A	B	C	D	E	F	G
0	PLANNING ISSUE	RMD 22/04/2026	TM 22/04/2026	JC 22/04/2026					

CONSULTANT
Fingleton White
Bridge Street Centre
Portlaoise
Co. Laois
Ireland
T:(00353)(0)57 866 5400
www.fingleton.ie

APPROVALS

A	DRAWING OFFICE	DRAWN BY R.McDONNELL
B	DESIGN ENGINEERING	CHECKED T.MALONE
C	STRATEGY/PLANNING	
D	DESIGN MANAGEMENT	APPROVAL J.CONROY
E	OPERATONS	
F	CONSTRUCTION	DATE 22/04/2026
G	AM/AO ADDITIONAL	

PROJECT
47327508 - Gas to Bord na Mona, Edenderry

TITLE
TEMPORARY CONSTRUCTION COMPOUND 03
GNI143 Ballykilleen Pipeline

Gas Networks Ireland

DRAWING NUMBER
GNI143-GNI-PL-TCC-0003

SCALE
AS STATED @A1

SHEET
01 OF 01

P.O Box 51, Gasworks Road, Cork, Rep of Ireland
T +353 21 4534000
